



TRIUNFO SANITATION DISTRICT

A PUBLIC AGENCY

Status of Conifer Tank Replacement Project TSD Board Meeting, December 19, 2011

Oak Canyon Reservoir

- Reservoir progress
 - Slurry cover for HDPE inlet/outlet piping
 - Overflow and drain line installed to intersect v-ditch
 - Potholing for Oak Hills completed
 - Tank pad liner and drain rock being installed
 - Perimeter forms for tank pad continuing
- Falling Star – CMWD required storage needs for turnout install
 - Waiting for intertie hydraulic analysis completion before exercising options
 - Double line stop and bypass around connection location
 - Use Cheeseboro Tank
 - Hot taps and line stops at connection
- Tie-in with Las Virgenes and Cal Water
 - AECOM preliminary hydraulic analysis nearly completed for Las Virgenes and will report recommendations and costs associated with this connection
 - AECOM is analyzing the Cal Water system and will report later this month
- Public Relations – no updates or changes

Lindero Feeder/Cheeseboro Tank Decommissioning

- Contract with Padre Associates for EIR and MND work is ready for Board review
- Staff developed a strategy for decommissioning the Lindero Feeder Line and the Cheeseboro Tank. A copy of this report is included in the Board packet

Conifer Tank Decommissioning

- Staff continued coordination efforts between the cell companies and the HOA for approval of the relocation plans and easement acquisition
- Staff is assisting the cell companies with their plan review and approval by the County of Ventura Planning Dept
- Staff developed a strategy for decommissioning the Lindero Feeder Line and the Cheeseboro Tank. A copy of this report is included in the Board packet

Financial Status of Project

- There are no changes to report at this time




Item 8a-1







**Triunfo Sanitation District
Oak Park Water Service
Conifer Tank Replacement Project Update**

December 2011

1a. Oak Canyon Reservoir : Tank View

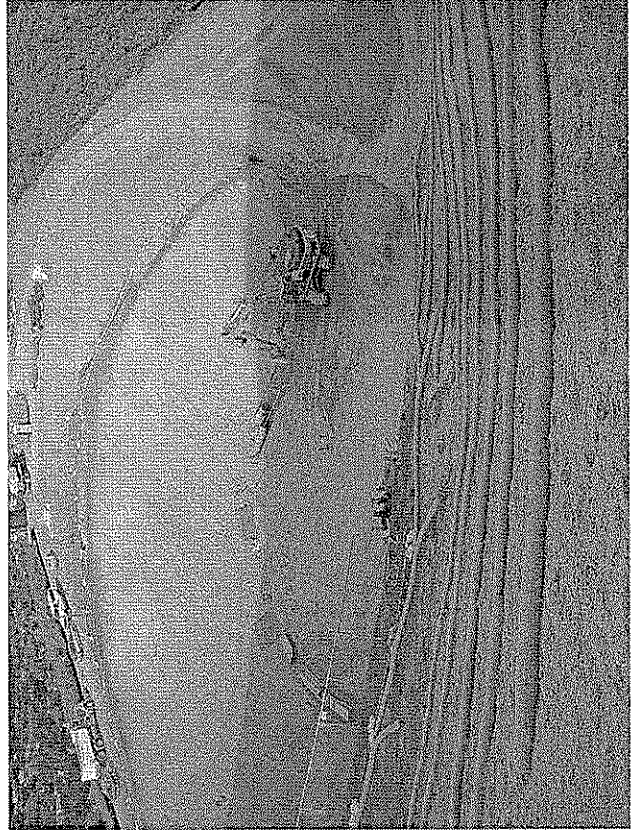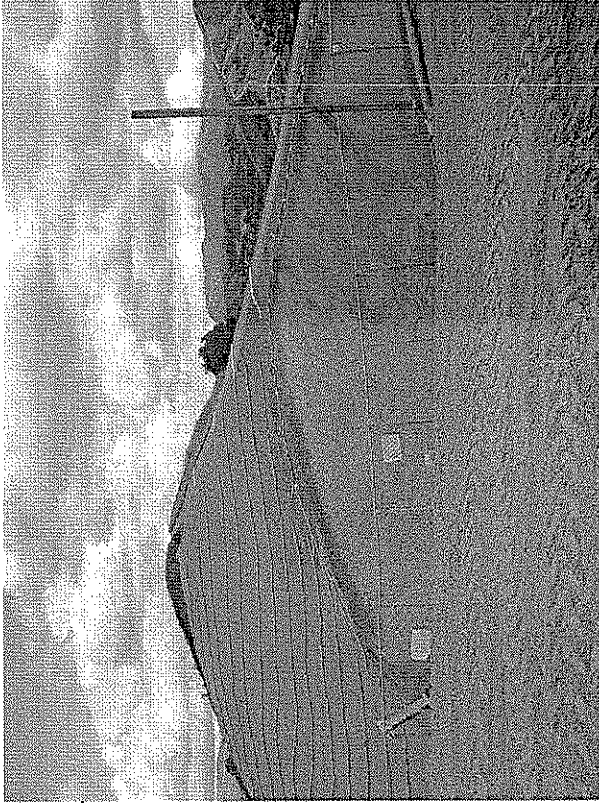

1b. Oak Canyon Reservoir : HDPE inlet/outlet

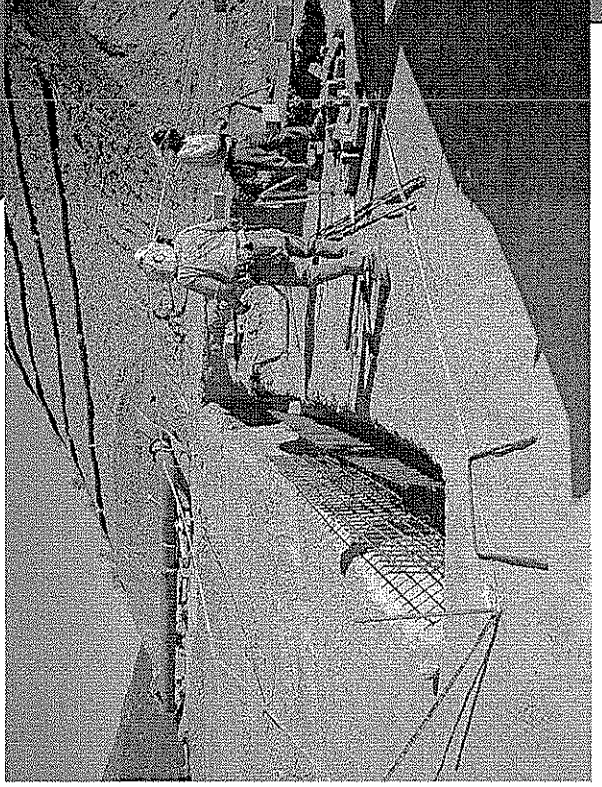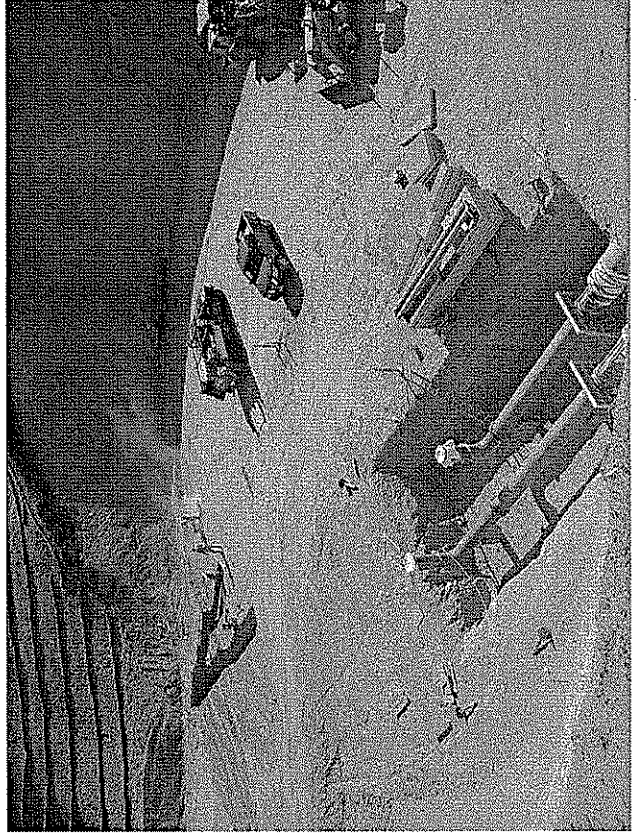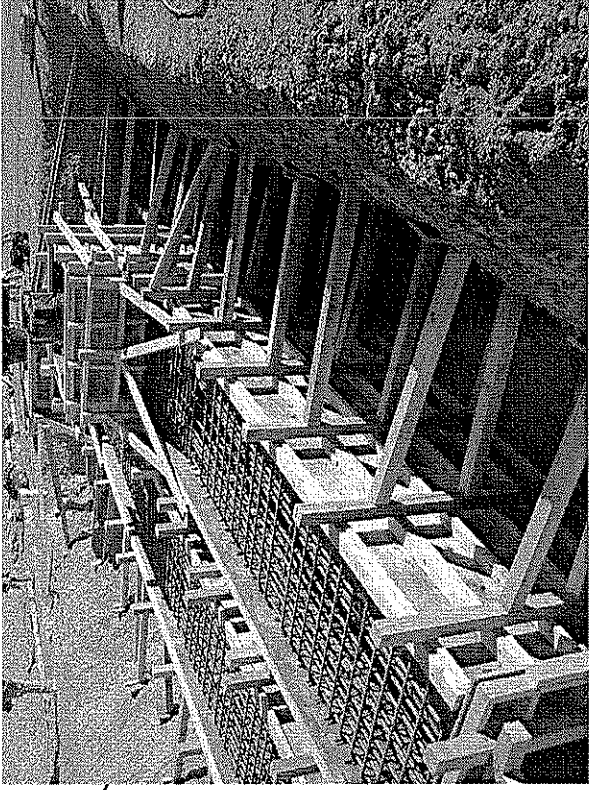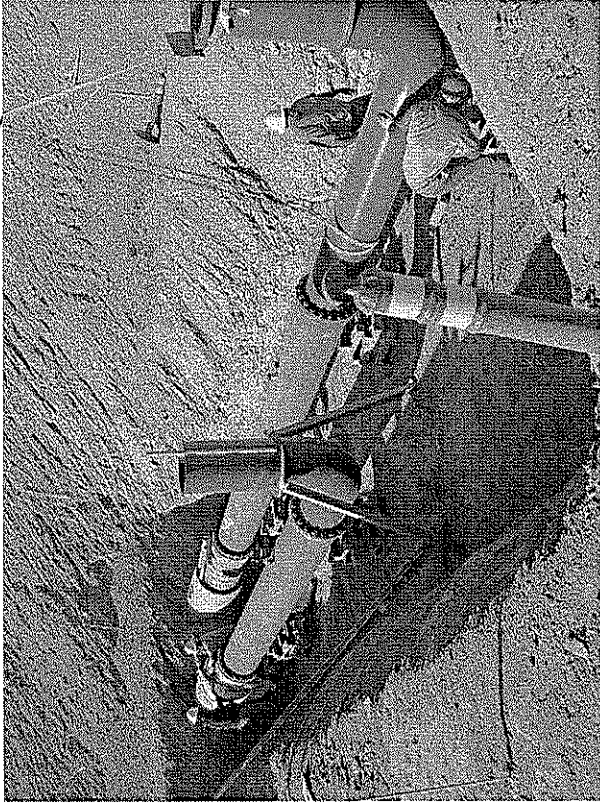

Oak Canyon Reservoir Schedule - Highlights

TASK	START DATE	EST. FINISH DATE
NOTICE TO PROCEED	6/27/11	
CONSTRUCTION PHASE	6/27/11	9/20/12
SITE GRADING PHASE 1	7/20/11	9/7/11
JACK AND BORE OPERATIONS	9/12/11	11/14/11
CONSTRUCT CONCRETE TANK	12/1/11	7/23/12
DYK CONCRETE TANK OPERATIONS	5/9/12	7/12/12
PIPELINE CONSTRUCTION 20" IN/OUTLET	7/13/12	7/24/12
GRADING OPERATIONS PHASE 2	7/13/12	8/17/12
SITE ACCESS ROAD	7/25/12	9/4/12
30" PIPELINE CONNECTION	8/1/12	8/1/12
PUNCHLIST	8/1/12	9/14/12
MISC. SITE IMPROVEMENTS	8/1/12	9/14/12
TSD FINAL WALK THROUGH	9/17/12	9/17/12
TANK IN OPERATION		9/20/12

8a-5

Board Updates/Revisions - Oak Canyon Reservoir

